VALUE-ENGINEERED · FULL DEVELOPMENT PACKAGE

CR 91
Park Plaza

One destination. Five phases.
A staged regional-destination plan designed to stay inside a disciplined capital envelope.

$40M–$50M

VALUE-ENGINEERED MASTER DEVELOPMENT

$5.5M

PHASE 1 WORKING FUNDING TARGET

Goodwater · County Road 91 corridor · Alabama

Planning update / 1 Nov 2026



Concept rendering

Documented regional visitation meets limited hospitality capacity.

DOCUMENTED REGIONAL VISITATION

238,302

Cheaha State Park guests in FY 2023-24

Cheaha spans Clay and Cleburne counties. The official count establishes a documented regional visitor base.

CR 91 adds dining, market, laundry and event capacity.

CLAY COUNTY EMPLOYMENT



23x employment-share gap

The mix signals limited local hospitality capacity, not a visitor count.

Sources: ADCNR FY 2023-24 Annual Report; Encyclopedia of Alabama; Clay County Chamber of Commerce.

Cheaha guests are not Clay County-only or CR 91 traffic. Route share and capture remain unverified.

DEFENSIBILITY

This site already has land control, operations and approval progress.

Those advantages would take a new entrant time to assemble.



~50 acres
Owned free and clear

25 sites
Operating RV park

Near final
Approval progress

~3,700 ft
Road frontage

PROPERTY DILIGENCE

Deed ownership is public record. Survey, engineering and septic diligence remain open.

PHASE 1 EXPERIENCE

One commercial anchor. Four reasons to stop.

A 7,200 SF plaza concentrates the first build around uses that can reinforce one another.



01

Restaurant

Daily lunch and dinner demand

02

Market

Convenience, coffee and prepared food

03

Laundry

Utility demand from residents and travelers

04

Event field

Markets, community events and seasonal visits

NOT IN PHASE 1 Later phases follow measured demand: lodging, water recreation and amphitheater concepts need separate feasibility, approvals and financing.

CUSTOMER CAPTURE

The working case requires about 225 customer actions per day.


Actions can overlap. A verified traffic and catchment denominator still has to prove the capture rate.

225

AVERAGE DAILY CUSTOMER ACTIONS

Illustrative working assumptions, not management forecasts.

ANNUAL CUSTOMER OCCASIONS BY USE · ILLUSTRATIVE

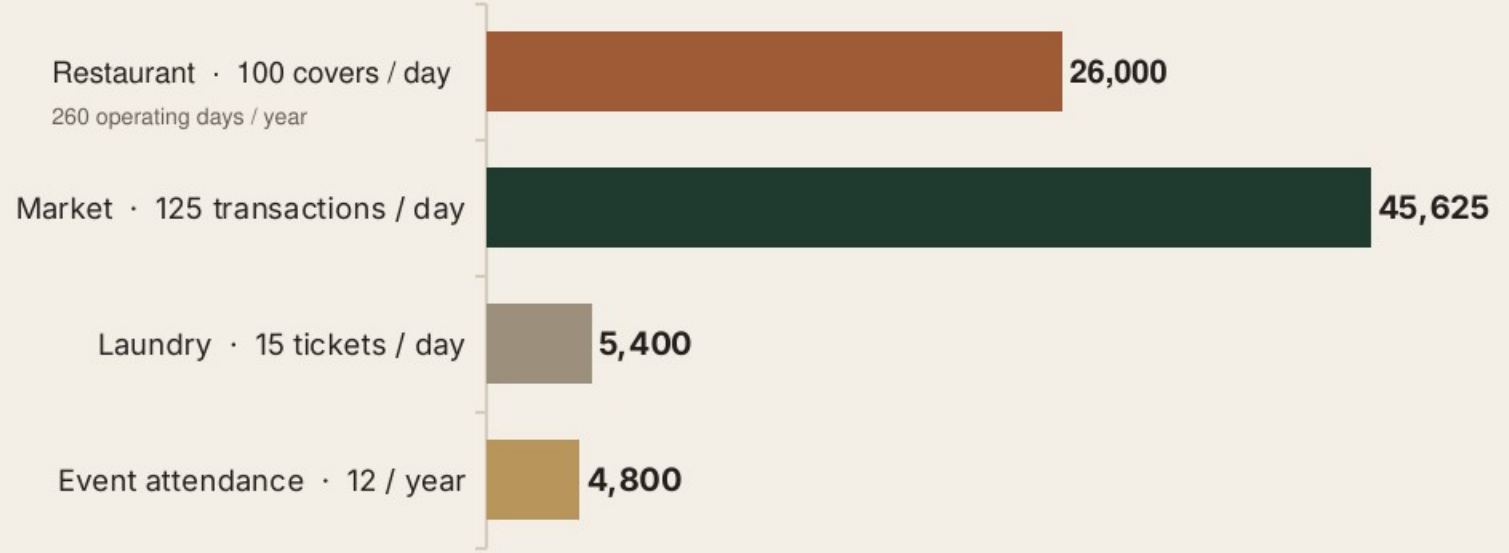

EVIDENCE REQUIRED

- ALDOT traffic counts
- 30-minute catchment
- RV occupancy
- Overlap between uses

Seasonal ride capacity and illustrative gross revenue

5 hours/day x 6 trips/hour x 10 seats x 10 vehicles x 30 days/month x 5 months

450,000 annual ride places at full modeled utilization

Utilization	Annual ride visits	$20 ticket revenue	$20 Plaza spend / visit	Combined gross
10%	45,000	$0.90M	$0.90M	$1.80M
30%	135,000	$2.70M	$2.70M	$5.40M
100% capacity	450,000	$9.00M	$9.00M	$18.00M

The 30% case means 900 ride visits per operating day. It is a utilization assumption, not a minimum attendance or revenue guarantee. Plaza spending assumes every ride visit generates $20 of purchases; actual capture and spend must be tested.

Operating requirement: six trips per hour means a 10-minute complete cycle, including loading and unloading. Confirm route length, vehicle capacity, turnaround, charging, staffing, safety and weather downtime. Counts represent visits, not unique people.

Prior Plaza-only working projection: $1.53M annual gross. Do not add the $2.7M visitor-purchase scenario to existing restaurant / market receipts without removing overlap. Ticket revenue is gross, before operating costs. Other event traffic is not modeled here.

Source: Elaine McNally email, 1 Nov 2026. Capacity, utilization and spending assumptions remain unverified.



Regional context image

WHY NOW

Nearby investment creates an opening window.

Westwater Resources is developing the Kellyton graphite processing plant nearby.

A TIMING FACTOR, NOT BASE DEMAND

Treat construction crews as opening-period upside, not permanent demand.

LOCAL COORDINATION

Coordination with county economic development and engineering contacts is underway.

$148K reported prior spend / ledger reconciliation pending
Historical spending is not new cash available at closing.

One package. Five phases. Designed to expand after demand is proven.

CR91 is being value-engineered as a regional destination that can open in stages, preserve future expansion pads and keep the full master-development plan inside a disciplined $40M-$50M capital range.

$40M-$50M
VALUE-ENGINEERED MASTER RANGE

01	02	03	04	05
Park Plaza	Glamping + Lights	Water Park	Cabins	Amphitheater
$5.5M	$0.5M-$1M	$25M-$30M	$0.75M-$1.5M	$2.5M-$4M
Immediate launch	Planned	Future	Future	Long-term

Shared site infrastructure, staged utilities, parking, landscaping, financing reserves and program contingency are planned at approximately $6M-$8M across the full buildout.

Future phases are intentionally value-engineered and expandable. The existing Real Nice & Easy RV Park remains a separate operating business outside this development capitalization.



PHASE 1 / PARK PLAZA

A $5.5M working funding target

Combined equity and lending, subject to final pricing and capital terms.

Cost to open	Preliminary use
Brooks construction	$3,304,000
Kitchen + corrected laundry carry	$481,000
Management / project support	$300,000
Operating reserve + buffer	$508,200
Itemized remaining owner / finance costs	$492,410
10% construction contingency	$330,400

$5,416,010 modeled uses / $83,990 target headroom

Equipment inclusions, utility scope, staffing and lender terms remain open. Light-show program is optional and excluded here. The reserve is retained, but its sufficiency requires monthly operating cash flow.

Glamping by the pond



Inspiration photo: cottonbro studio / Pexels. Photo depicts another setting, not the CR 91 property.

Five sites identified around the pond feature, among the flower beds.

A proposed lodging addition alongside the operating 25-site RV park. Glamping would offer an outdoor stay for guests who do not bring an RV.

DEVELOPMENT REQUIREMENT

The sites are not yet developed. Bathroom facilities are needed before development can proceed.

PARTNERSHIP OPPORTUNITY

Explore glamping development and operating partners. Unit design, infrastructure costs, financing and opening timing remain to be determined.

The signature light-show experience

Conceptual visualization currently featured on CR91.com



CONCEPTUAL DEVELOPMENT STUDY · FUTURE PLANS AND IMAGERY SUBJECT TO CHANGE

PRELIMINARY PROGRAM BUDGET

$238.8K

FOUNDER-SUPPLIED ESTIMATE

Light displays	$100,000
Transportation	$40,000
Concrete	$20,000
Installed storage building	$40,000
Trail / pad / berm sitework	$38,800

INVESTOR TREATMENT

Optional program, outside the core Phase 1 cost model.
If fully incremental: $5.655M total, $154.8K above $5.5M.
Confirm fleet capacity, installed quotes and scope overlaps.



PHASE 03

Water Park & Adventure

VALUE-ENGINEERED REGIONAL ATTRACTION

$25M–$30M

TARGET ALL-IN DEVELOPMENT CAP

A regional family-recreation anchor designed around a hard all-in budget cap rather than the largest possible attraction package.

- WhiteWater will be asked to redesign the attraction mix so equipment, pools, filtration, buildings, civil work, parking, installation and contingency can fit the $25M-$30M total target.
- Opening scope can prioritize 2-3 headline slide attractions, a family play structure, a modest river / activity-water component and children's splash features, with expansion pads preserved.
- The current $16.877M interim equipment arithmetic is too high for this cap and must be reduced; final attraction mix, engineering and installed cost remain subject to WhiteWater and civil review.

Illustrative concept image. CR91 is intentionally value-engineering the opening waterpark and preserving room to add attractions after attendance is proven.



PHASE 04

Cabins & Accommodations

SMALL FIRST COLLECTION · EXPANDABLE

$0.75M–$1.5M

VALUE-ENGINEERED OPENING RANGE

A small first collection of cabins designed to add a non-RV overnight option without overbuilding lodging before demand is proven.

- Initial target: approximately 5 cabins / cottages, with the ability to expand toward 10 later.
- CR91 can pursue discounted / relationship-based construction while keeping utilities, access, drainage, furnishings and permitting in the budget.
- Additional units would be added only after occupancy and event / waterpark demand support expansion.

Illustrative concept image. The opening budget assumes a small, practical cabin collection rather than a full resort-lodging buildout.



PHASE 05

Event Lawn & Amphitheater

PHASE A VENUE · EXPANDABLE

$2.5M–$4M

VALUE-ENGINEERED OPENING RANGE

An outdoor event lawn with a permanent covered stage, mixed lawn / chair capacity and practical guest infrastructure - built to host regional events before investing in a full touring amphitheater.

- Keep the current ~2,800-3,000 mixed-capacity vision, but open with a simplified stage, lawn seating and limited permanent seating.
- Stage AV / lighting, restrooms, concessions and backstage support stay practical; parking can combine paved core spaces with lower-cost overflow where permitted.
- Future upgrades can add fixed seating, premium production, VIP, larger backstage and additional paved parking after event demand is proven.

Illustrative concept image. This opening phase is intentionally smaller than a fully built touring-concert amphitheater.

Approximately $46M in working phase allocations

$40M-$50M remains the value-engineering range for the full destination. Later-phase figures are planning allowances, not current all-in bids.

Phase / package	Working allocation	Planning range / status
Phase 1 / Park Plaza	$5.50M	$5.5M working funding target
Phase 2 / Glamping + lights	$0.75M	$0.5M-$1M early allowance
Phase 3 / Water park	$28.00M	$25M-$30M value-engineering target
Phase 4 / Cabins	$1.10M	$0.75M-$1.5M early allowance
Phase 5 / Amphitheater + events	$3.50M	$2.5M-$4M early allowance
Shared infrastructure / reserves	$7.00M	$6M-$8M preliminary
Working allocation total	$45.85M	Approximately $46M

Reconcile shared infrastructure and contingency across phase budgets before adding them. The optional $238.8K light-show program is part of the later-scope discussion, not a second addition to both phases. Existing RV operations remain a separate entity.

Equity and conditional lending must close together

Phase 1 needs a coordinated $5.5M funding plan. Debt, equipment finance and outside equity are components of that total, not extra proceeds above it.

01 Define the required equity

Ask each lender for the equity injection, eligible costs, collateral, guarantees and conditions needed for the Phase 1 scope.

02 Obtain written lender terms

Request a dated conditional commitment or term sheet specifying the amount, expiry, equity condition and remaining underwriting requirements. No commitment is claimed in this deck.

03 Match investor and lender conditions

Coordinate escrow, funds verification and closing sequence so each party understands what the other must deliver. Do not describe expressions of interest as committed funds.

04 Underwrite later phases separately

The light-show scenario and future attractions need their own operating proof, approvals and reconciled budgets before capital is deployed.

The pro forma uses $2.5M of hypothetical debt only to illustrate fees and construction interest. It does not establish an approved debt amount or the required angel investment.

Four workstreams determine how quickly the $40M-$50M master program becomes financeable.

The goal is a disciplined, expandable destination: prove Phase 1, lock value-engineered scope, and replace management allowances with vendor quotes and engineering before each later phase is financed.

01

Equity commitments

Close the Phase 1 outside equity gap and document sponsor capital. Future phases can be capitalized as their underwriting matures.

02

Final bids + engineering

Replace planning allowances with contractor bids, survey, engineering, permits and value-engineered vendor scopes - including a redesigned WhiteWater package capped at $25M-$30M all-in.

03

Cash flow proof

Demonstrate Phase 1 standalone debt service from Plaza, events and operating assumptions before relying on future phases.

04

Land + entity clarity

Approx. 50 acres are owned outright/free and clear at the landowner level. Any project-company ground lease must be described as internal structure, not third-party site control.

This is a master capital-planning package. Future phases remain subject to feasibility, value engineering, approvals, operating strategy and financing.

Why CR91 - and why this structure now?

The opportunity is not to finance every future attraction on day one. It is to use a controlled site and an operating foundation to prove demand, then deploy larger capital only when each phase earns it.

TWO-SENTENCE INVESTMENT THESIS

CR91 is a staged hospitality and regional-entertainment development built on approximately 50 acres already controlled by the sponsor, alongside an operating 25-site RV business, with Phase 1 designed to establish cash flow before later capital-intensive attractions are funded.

Value is created by adding missing dining, convenience, lodging, recreation and

~50 ACRES

Site control

Owned free and clear at the landowner level; survey, engineering and entity documentation continue.

25 SITES

Operating foundation

Existing RV operation provides a real site use and operating base before the Plaza launches.

238,302

Regional visitation

Official Cheaha State Park FY 2023-24 guest count establishes documented regional visitor activity.

5 PHASES

Capital optionality

Each later phase can be re-underwritten, reduced, delayed or expanded as evidence improves.

DIFFERENTIATION · Existing land + operating RV use + phased underwriting + a value-engineered cap create optionality that a single-shot greenfield build does not have.

RETURN DRIVERS + ASSUMPTIONS

Where value can come from - and what still has to be proven.

CR91 should separate execution-dependent value creation from market-dependent assumptions. Investor return terms remain open; no IRR, preferred return or equity multiple is implied in this working package.

$1.53M

PROJECTED PHASE 1 ANNUAL GROSS

Base restaurant + market + laundry + event fees; excludes existing RV revenue and seasonal light-show tickets.

225

WORKING DAILY CUSTOMER ACTIONS

Illustrative requirement across uses; actions can overlap and the capture denominator remains unverified.

$25M-$30M

PHASE 3 ALL-IN CAP

Waterpark target requires vendor value engineering; scope is reduced or delayed if it cannot fit the cap.

EXECUTION-DEPENDENT VALUE

Phase 1 operations	Open the Plaza around a $5.5M working capital target.
Customer capture	Convert regional / local demand into repeat restaurant, market, laundry and event use.
Phased deployment	Do not finance later attractions until updated demand, scope and capital terms support them.
Value engineering	Reduce or defer non-core scope instead of protecting an oversized concept at any cost.

MARKET / FINANCING ASSUMPTIONS TO PROVE

Traffic + catchment	ALDOT traffic, drive-time catchment, RV occupancy and overlap between uses.
Construction certainty	Contractor bids / GMP must replace allowances before the close.
Operator economics	Restaurant operator, staffing plan and unit P&L remain key credibility unlocks.
Cost of capital	Debt pricing, leverage and equipment financing affect free cash flow and investor economics.

DOWNSIDE EXECUTION PLAN

If the base case misses, the response is to preserve liquidity and optionality.

These are management actions, not guarantees. Exact covenants, reserves and decision rights will be documented with lenders, investors and operators before closing.

STRESS / TRIGGER	CR91 RESPONSE
Phase 1 construction runs 10%-15% above plan	Rebid and value-engineer nonessential scope; use contingency deliberately; defer later-phase spending; do not protect schedule by quietly expanding the master cap.
Opening or customer ramp is slower than planned	Preserve the six-month operating reserve, reduce variable launch spend, prioritize proven revenue uses and delay Phase 2 / Phase 3 capital until operating evidence improves.
Debt pricing or leverage becomes less attractive	Rebalance debt/equity, keep equipment financing separate where useful and delay the close rather than force an unsustainable debt-service burden onto Phase 1.
Waterpark cannot be delivered inside $25M-$30M all-in	Reduce attractions / civil scope, preserve expansion pads or postpone Phase 3. The development cap governs the attraction package - not the reverse.

GUARDRAILS: $462K six-month operating reserve + $46.2K buffer / $330.4K modeled construction contingency / staged later-phase capital

Funding target and financing sources

The $5.5M Phase 1 working target is a combined sources-and-uses framework. No lender approval, equity commitment or final investor economics is implied.

Source / use	Current treatment
Total Phase 1 funding target	$5.5M combined capital, subject to pricing and terms
Senior debt + equipment finance	Amounts and eligible costs to be established with lenders
Outside angel / partner equity	Required amount depends on actual lender conditions and verified closing sources
Founder historical spending	$148K reported as of October; ledger and treatment pending. Not fresh closing cash.
Management and project support	$300K allowance included in uses. Final scopes, payees and payment timing remain open.

Terms required before investor close

Ownership, preferred return, return of capital, profit split, distribution timing, governance, future-phase rights and exit provisions require definitive agreements. No IRR, guaranteed return or negotiated waterfall is presented as approved.

The strongest investor objections should be addressed directly - not buried in diligence.

CR91 is stronger when the pitch distinguishes what is already supported from what still needs evidence.

01

Rural location / capture is not yet proven

CURRENT RESPONSE

Documented Cheaha visitation and the operating RV site establish regional activity, but CR91 still needs ALDOT traffic, drive-time catchment and overlap analysis before claiming a verified capture rate.

02

Five phases create execution complexity

CURRENT RESPONSE

The master plan is not a one-close construction commitment. Phase 1 launches first; every later phase has a value-engineered range, a stage gate and the option to shrink, delay or expand.

03

Construction costs are still planning allowances

CURRENT RESPONSE

That is a real closing risk. Contractor bids, engineering, survey and ultimately a lender-acceptable GMP / cost package are explicit readiness requirements - not assumed away.

04

Restaurant / operating execution is still open

CURRENT RESPONSE

Operator selection, unit P&L, staffing plan and continuity terms are identified as one of the largest Phase 1 credibility unlocks and should be resolved before final underwriting.

INVESTOR-READY RESPONSE · State the objection plainly → show the evidence already in hand → identify the exact diligence item that closes the remaining gap.



PROJECT OWNER

Elaine McNally

Founder and sole accountable owner

Site vision, local relationships, approvals and project leadership.

IMMEDIATE OWNER DECISIONS

Confirm equity terms
Confirm parcel county
Advance operator selection

WORKING TEAM

Supporting roles, not co-owners.

Devon Archer

FINANCE AND CAPITAL STACK

Unit economics, sources and uses, lender case and investor diligence.

Jonathan Avila, PE

Avila Engineering Group

SEPTIC ENGINEERING & PERMITTING

Planned engagement upon funding. Septic layout and health-department permitting depend on the topo survey and final scope.

GC and design team

DELIVERY

Not yet documented as committed

GMP, schedule, contingency and construction execution.

Restaurant operator

OPERATIONS

To be selected

Menu, staffing, P&L, opening plan and daily execution.

GC/design commitments and restaurant operator selection remain open.

THE CAPITAL OPPORTUNITY

Invest in the first phase. Preserve optionality across the full destination.

$5.5M

PHASE 1 WORKING FUNDING TARGET

$40M–$50M

VALUE-ENGINEERED MASTER RANGE

CR91 is seeking strategic equity and debt partners for a staged development plan that puts Phase 1 cash flow, downside discipline and documented investor alignment ahead of later-phase expansion.

Immediate priorities

1 Document Phase 1 equity economics
2 Finalize contractor bids + operator
3 Complete capture / downside work
4 Re-scope waterpark to the all-in cap

Planning materials only. Not an offering memorandum. Final securities terms require counsel.
